



Daily Report

HAHN ARROYO PROJECT - PHASE 1 - 2011

REPORT DATE	5/4/11	PRIME CONTRACTOR	RMCI
COA PROJ. NO.	527481	SUB-CONTRACTORS	Guzman, Advantage, PRS
REPORT NO.	78	PROJECT MANAGER	Jim Spinello
AMAFCA PROJ. NO.	400 154001	OTHER INSPECTOR(S)	Rhonda Hice

DAY 108 OF 247 CALENDAR DAYS (CO #2 added 7 Cal Days)

DAY 108 OF 127 CALENDAR DAYS BID LOT NO. 2 (CO #2 added 7 Cal Days)


CONTRACTOR WORK HOURS: 7:30 am - 4:30 pm

HOURS OBSERVED: 8:00 to 9:30 am and 2:00 to 4:00 pm

WEATHER: Clear 49°F -80°F

VISITORS ON SITE: Vinyard

WORK DESCRIPTION: RMCI forming sill wall along the north side of the channel from Sta 11+00 to 13+30 Lt. Crew also working fine grade between Sta 9+00 and 8+00 and placing top forms. Guzman moved back to the BOP removing the last of the concrete channel lining and fixing rough grade the last 100' of channel. PRS tying rebar at the WQS. Superior not on site today. Will be placing shotcrete tomorrow at the WQS.

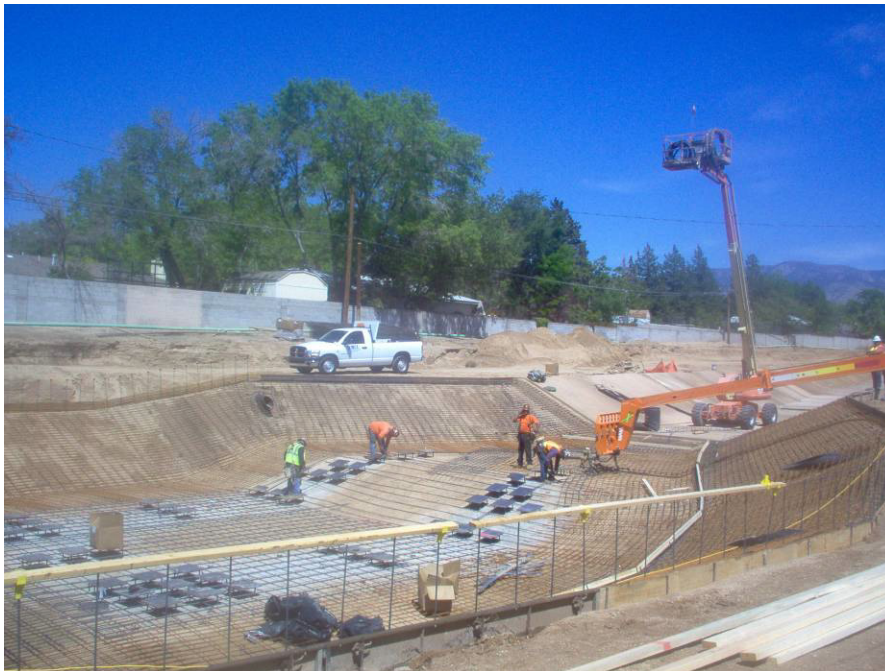

PRS tying rebar at the WQS.
Superior will be placing shotcrete tomorrow.



RMCI forming sill wall from Sta
13+30 to 11+00 Lt
