



Daily Report

HAHN ARROYO PROJECT – PHASE 1 – 2011

REPORT DATE	5/20/11	PRIME CONTRACTOR	RMCI
COA PROJ. NO.	527481	SUB-CONTRACTORS	Advantage, Guzman
REPORT NO.	90	PROJECT MANAGER	Jim Spinello
AMAFCA PROJ. NO.	400 154001	OTHER INSPECTOR(S)	Rhonda Hice

DAY 124 OF 253 CALENDAR DAYS (added by CO #3 – 6 calendar days)

DAY 124 OF 133 CALENDAR DAYS BID LOT NO. 2 (added by CO #3 - 6 calendar days)

CONTRACTOR WORK HOURS: 7:30 am- 4:30 pm

HOURS OBSERVED: 8:00 to 9:00 am and 12:30 to 2:30 pm


WEATHER: pt cloudy 48°F -69°F

VISITORS ON SITE: Vinyard

WORK DESCRIPTION: RMCI prepared MH base at Sta 5+79. Also prepared subgrade for the rundown at 6+50 LT. Crews working in the park putting up construction fence and cutting down the 2 ash trees as previously discussed. Indian Investors mob'bed their backhoe but will not start work until Monday.



RMCI setting up work area with orange fencing and tree removal.

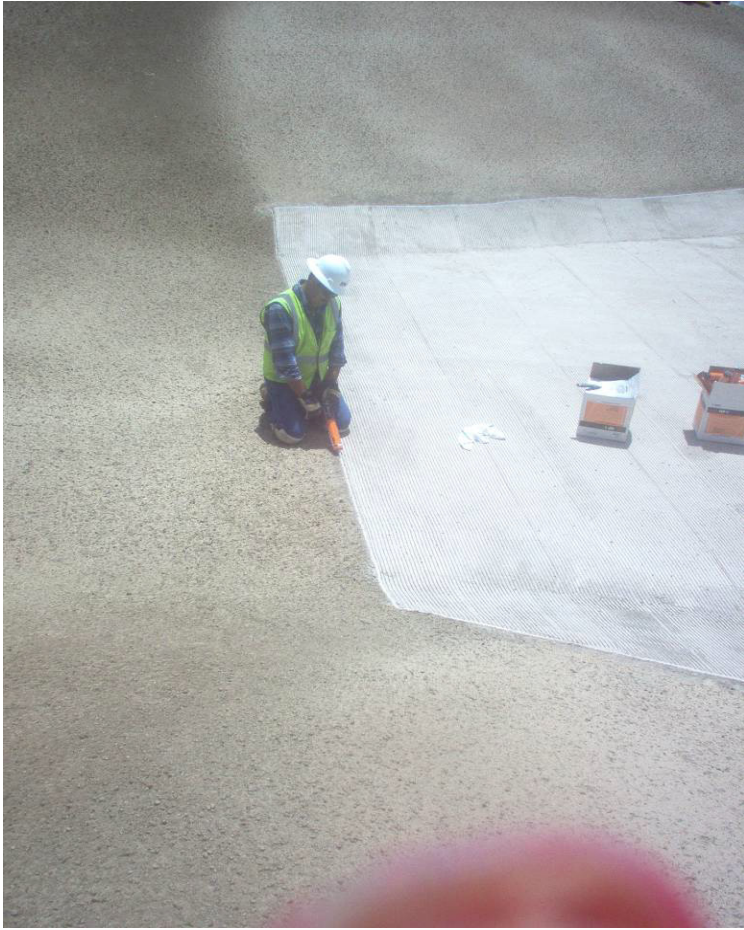

RMCI placing NP-1 color Tan at WQS.
